


ID	Task Name	Start	Finish	Duration	May	July	September	November	January	March	May	July	September	November	January	March
					M	J	S	N	J	M	M	J	S	N	J	M
1	<b>Module 3 - Feasibility Study</b>	Thu 5/22/14	Thu 5/22/14	1 day												
2	SBNC - Approval of Preliminary Design Program (PDP)	Mon 6/2/14	Mon 6/2/14	1 day												
3	Preliminary Design Program (PDP) to MSBA	Fri 6/6/14	Fri 6/6/14	1 day												
4	MSBA Review of PDP	Fri 6/6/14	Fri 6/20/14	11 days												
5	Project Team Revise PDP and create PSR	Fri 6/20/14	Mon 8/4/14	32 days												
6	SBNC - Approval of Project Schematic Report	Mon 8/4/14	Tue 8/5/14	2 days												
7	Project Schematic Report (PSR) to MSBA	Thu 8/7/14	Thu 8/7/14	1 day												
8	MSBA Review of PSR	Fri 8/8/14	Tue 8/19/14	8 days												
9	Facility Assessment Subcommittee Meeting	Wed 8/20/14	Wed 8/20/14	1 day												
10	REVISED Project Schematic Report (PSR) to MSBA	Thu 10/16/14	Thu 10/16/14	1 day												
11	Facility Assessment Subcommittee Meeting	Wed 10/29/14	Wed 10/29/14	1 day												
12	MSBA Board Meeting - PSR Approval	Wed 11/19/14	Wed 11/19/14	1 day												
13	<b>Module 4 - Schematic Design</b>															
14	SD Submittal Development	Thu 11/20/14	Wed 4/15/15	105 days												
15	SBNC Approval of Schematic Design & Budget	Mon 3/16/15	Mon 3/16/15	1 day												
16	SD Notification Email Sent to MSBA	Thu 4/2/15	Thu 4/2/15	1 day												
17	SD Submittal Date to MSBA	Thu 4/16/15	Thu 4/16/15	1 day												
18	MSBA Review	Fri 4/17/15	Fri 5/15/15	21 days												
19	Address SD Comments	Mon 5/18/15	Tue 6/2/15	12 days												
20	MSBA Board of Directors Approval of PSB	Wed 6/3/15	Wed 6/3/15	1 day												
21	<b>Module 5 - Funding the Project</b>															
22	City of Pittsfield, City Council PSB Approval	Tue 4/14/15	Tue 4/14/15	1 day												
23	Certificate of Vote Sent to the MSBA	Wed 4/15/15	Tue 4/28/15	10 days												
24	Project Funding Agreement Executed	Thu 6/4/15	Wed 6/24/15	15 days												
25	<b>Module 6 - Detailed Design</b>															
26	Massachusetts Historical Commission (MHC) File Project Notification Form (PNF)	Fri 5/29/15	Thu 7/9/15	30 days												
27	Submission of CMr Application to IG Office (up to 60 days)	Tue 5/19/15	Fri 6/12/15	19 days												
28	Construction Manager Selection Process	Mon 6/15/15	Fri 7/31/15	35 days												
29	Subsustainable Design, Project Registration	Mon 6/15/15	Mon 6/15/15	1 day												
30	Provisional Review Submittal	Mon 6/3/19	Mon 6/3/19	1 day												
31	Final Review Submission	Wed 6/1/16	Wed 6/1/16	1 day												
32	Design Development	Fri 5/1/15	Fri 7/31/15	66 days												
33	Cost Estimate / Reconciliation	Mon 8/3/15	Thu 9/3/15	24 days												
34	<b>DD Submission Date to MSBA</b>	Thu 9/3/15	Thu 9/3/15	1 day												
35	MSBA DD review	Thu 9/3/15	Thu 10/1/15	21 days												
36	Address DD Review Comments	Thu 10/1/15	Thu 10/29/15	21 days												
37	60% CD Development	Thu 9/3/15	Mon 1/4/16	88 days												
38	Cost Estimate / Reconciliation	Mon 1/4/16	Mon 2/1/16	21 days												
39	<b>60% CD Submission Date to MSBA</b>	Thu 2/4/16	Thu 2/4/16	1 day												
40	MSBA 60% CD Review Comments	Thu 2/4/16	Fri 3/4/16	22 days												







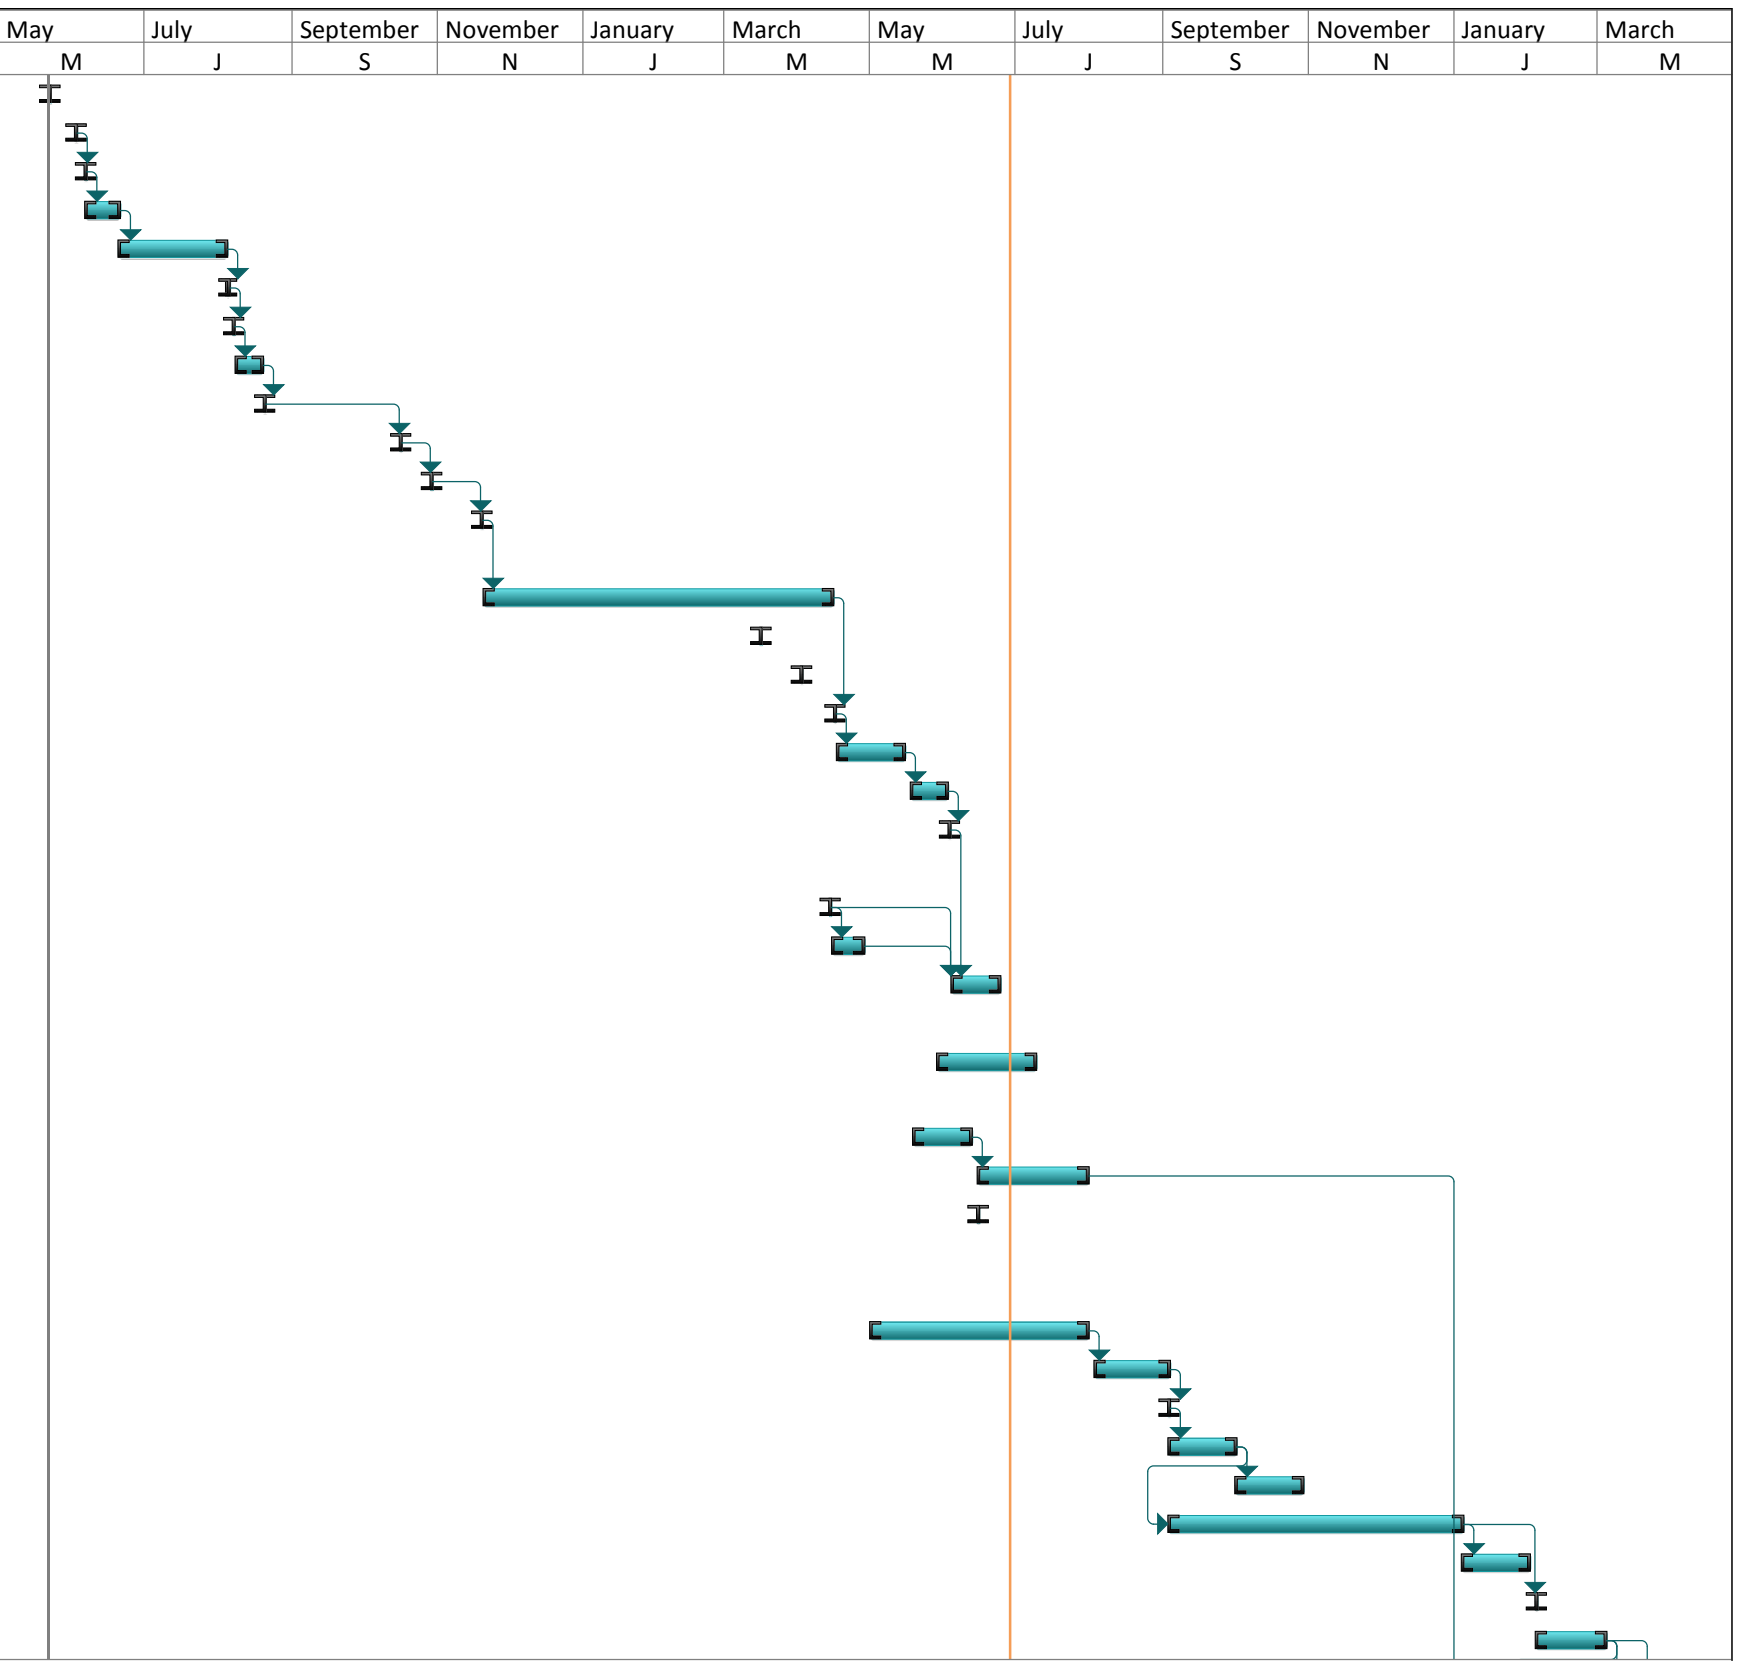













Project: Pittsfield Project Schedule Date: Mon 6/29/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


ID	Task Name	Start	Finish	Duration	May	July	September	November	January	March	May	July	September	November	January	March
					M	J	S	N	J	M	M	J	S	N	J	M
41	Address 60% Review Comments	Fri 3/4/16	Fri 4/1/16	21 days												
42	90% CD Development	Thu 2/4/16	Tue 3/22/16	34 days												
43	Cost Estimate / Reconciliation	Tue 3/22/16	Thu 4/21/16	23 days												
44	<b>90% CD Submission Date to MSBA</b>	Thu 4/21/16	Thu 4/21/16	1 day												
45	MSBA 90% CD Review Comments	Fri 4/22/16	Fri 5/20/16	21 days												
46	Address 90% Review Comments	Fri 5/20/16	Thu 6/16/16	20 days												
47	<b>100% CD / Bid Package</b>	Thu 6/16/16	Thu 6/16/16	1 day												
48	Addenda Period	Fri 6/17/16	Thu 6/30/16	10 days												
49	Filed Sub Bid Process	Thu 6/16/16	Fri 7/29/16	32 days												
50	GMP Final	Fri 7/29/16	Fri 7/29/16	1 day												
51	<b>Module 7 - Construction Administration</b>															
52	NTP Early Package Release, Site Work, Foundation, etc.	Fri 1/1/16	Tue 3/1/16	43 days												
53	Steel Erection / Topping off	Fri 3/31/17	Fri 3/31/17	1 day												
54	Building Water Tight	Mon 7/3/17	Mon 7/3/17	1 day												
55	Substantial Completion	Fri 6/29/18	Fri 6/29/18	1 day												
56	Move-in	Mon 7/2/18	Mon 9/3/18	46 days												
57	Demolition of Existing Building	Mon 7/2/18	Fri 12/28/18	130 days												
58	Access Roads / Final Seeding	Tue 1/1/19	Mon 4/1/19	65 days												
59	<b>Module 8 - Project Closeout</b>															
60	Final Completion / Project Closeout	Mon 4/1/19	Mon 7/1/19	66 days												

Project: Pittsfield Project Schedule Date: Mon 6/29/15	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

March	May	July	September	November	January	March	May	July	September	November	January	March	May	July	September	November	January	March	May	July	S
M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	
<div style="display: flex; justify-content: space-between; width: 100%;"> <span>I</span> <span>I</span> </div>																					

Project: Pittsfield Project Schedule  
Date: Mon 6/29/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

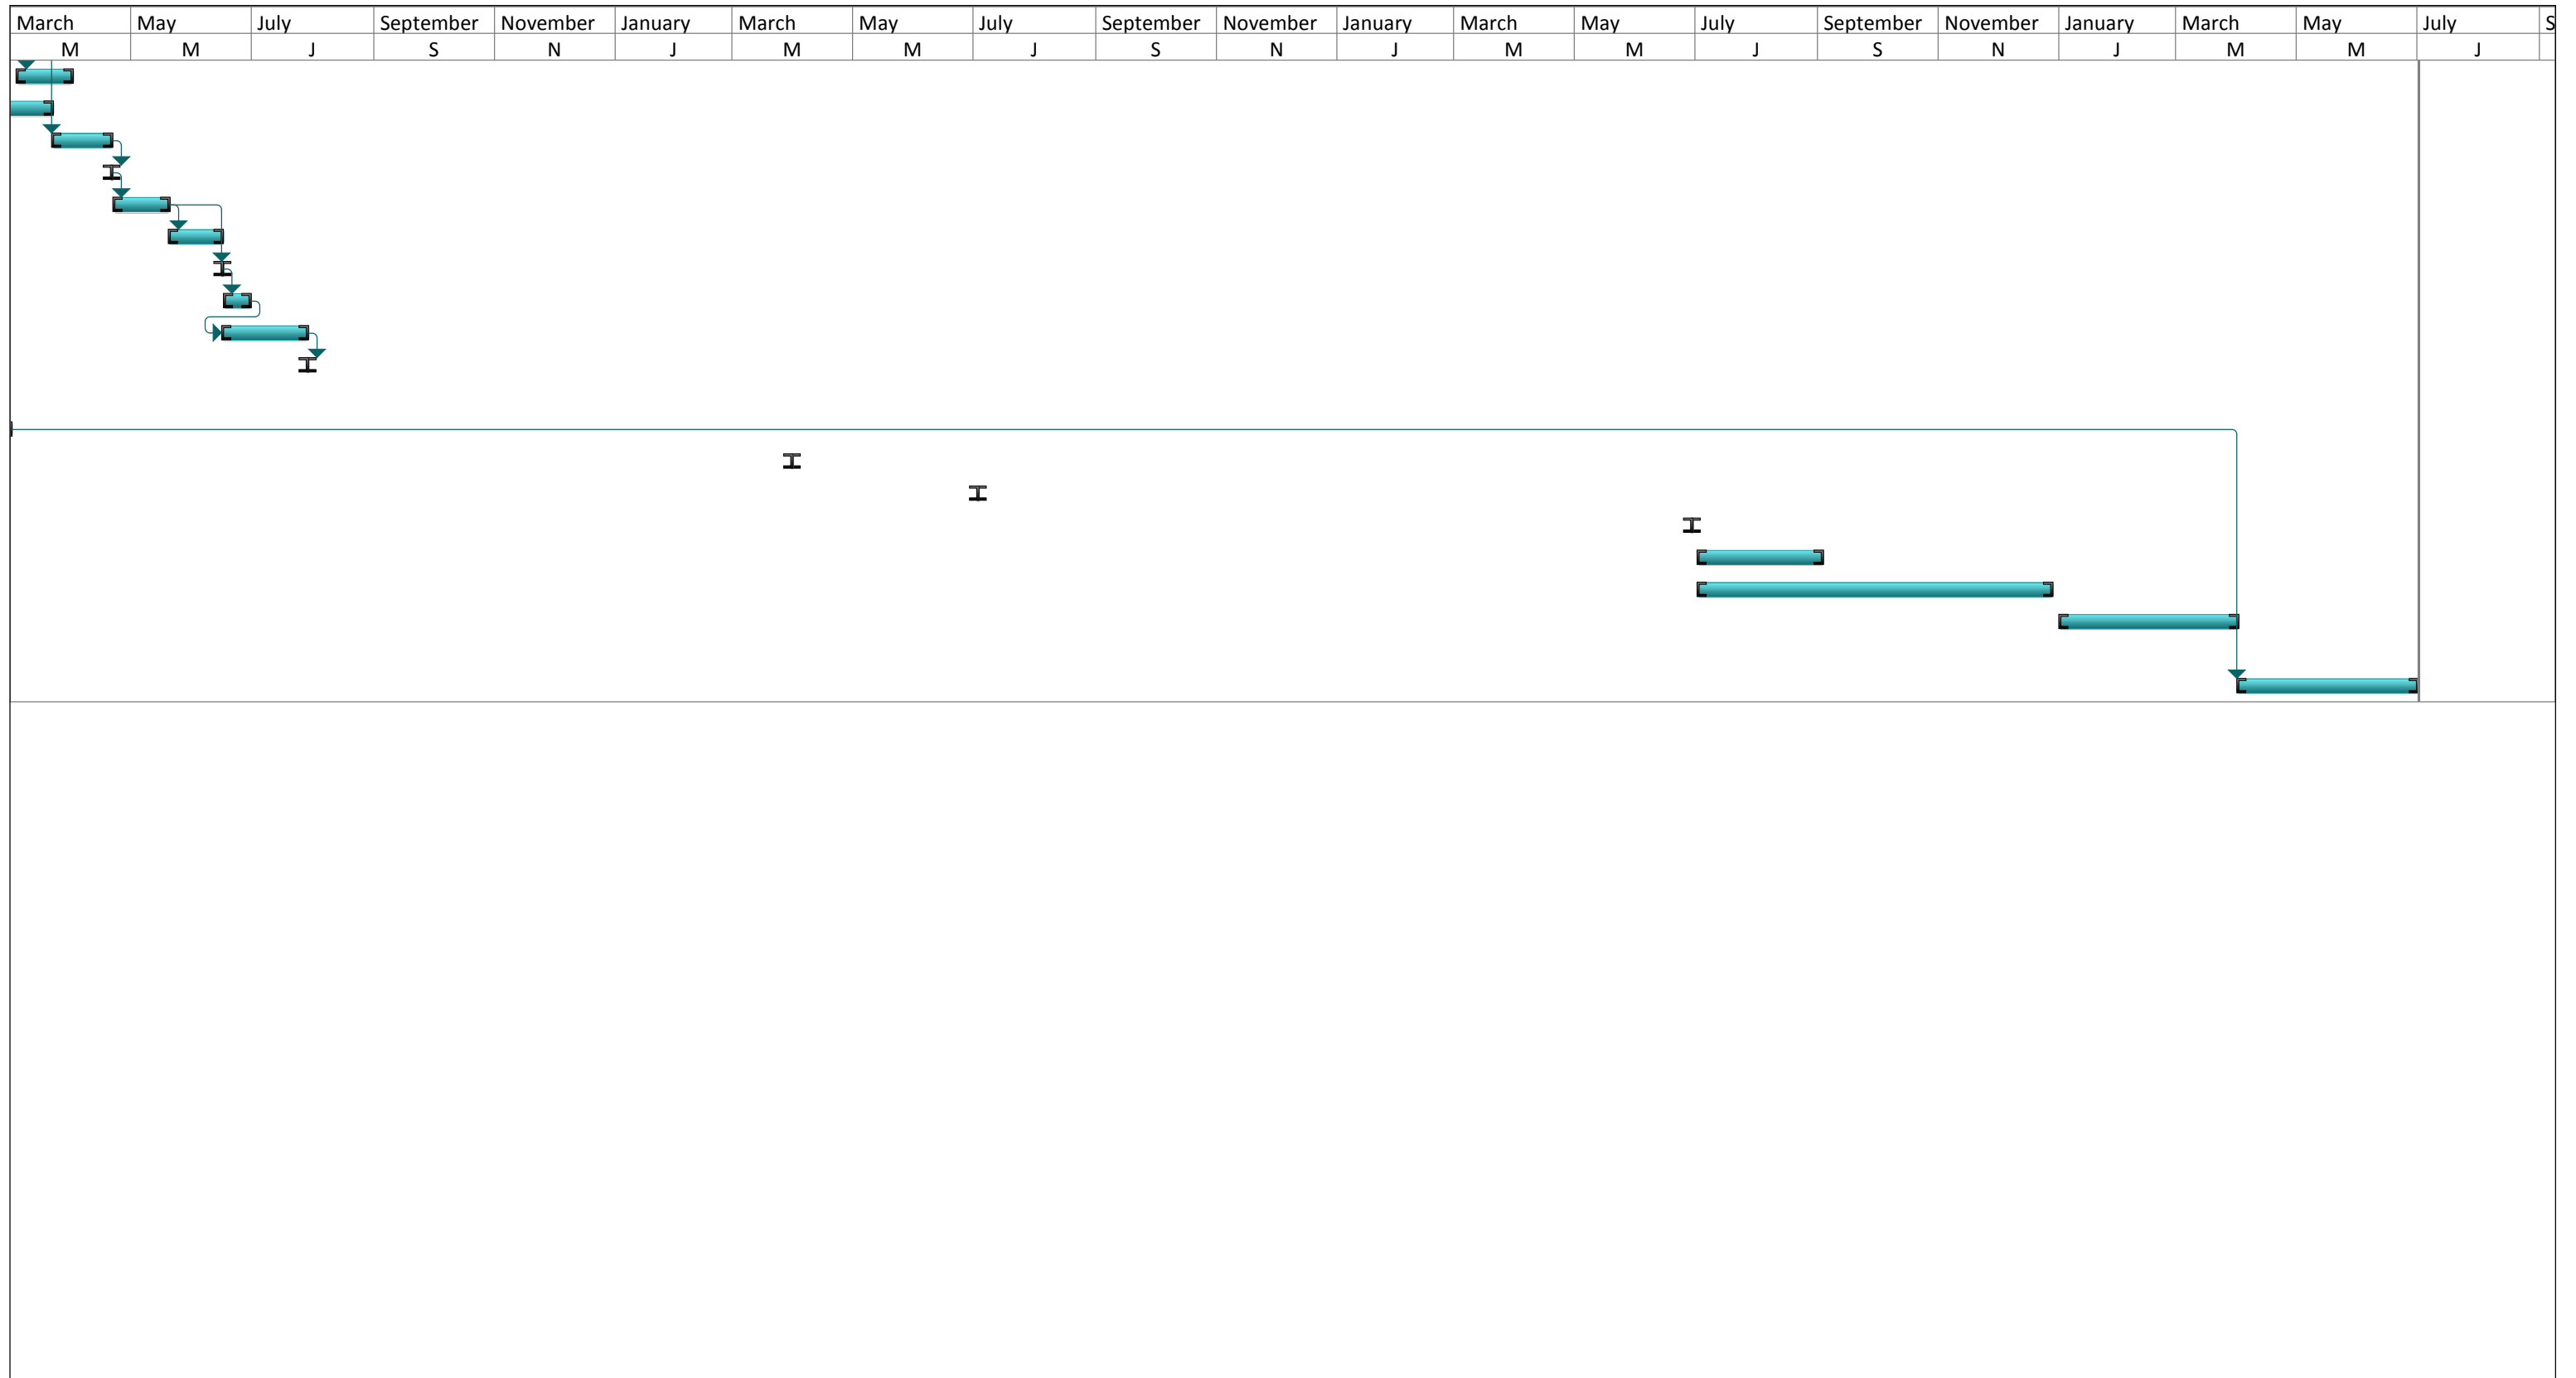

Project: Pittsfield Project Schedule  
Date: Mon 6/29/15

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
